Title:

FABRICATION PLAN FOR BEAM SPLITTER CHAMBERS (BSC)

FABRICATION PLAN

FOR

BEAM SPLITTER CHAMBERS (BSC)

LIGO VACUUM EQUIPMENT

Hanford, Washington and Livingston, Louisiana

Livingston, Louisiana								
QUA MAI TEC	EPAREI ALITY A NUFAC CHNICA DJECT A	ASSUI TURI AL DII	NG EN	GINEER:	Phi Ala Phi D. C Ru	MOFBI MAD FAI	Work of leaving Land	
Information coused only as re	ontained in equired to	n this sp respond	ecification	n and its atta ecification re	chments is propr equirements, and	rietary in natur I shall not be d	e and shall be kept confidential. I isclosed to any other party.	t shall be
								
ø	PEF	SIPE	Dma	w	ISSUE FF	R DED	DIGI FOR FOR	
REV LTR.	BY-D	I		D. DATE			CRIPTION OF CHANGE	
ROCESS SYSTEMS INTERNATI				ERNATI	ONAL, INC.		SPECIFICATIO	N
INITIAI APPROVA	l	PREPA PSF	RED	DATE 5/1/16	APPROVED RES	DATE \$/2/96	NumberA V049-2-080 μςο-ε960162-00-V	Rev.

TABLE OF CONTENTS

- 1.0 Purpose
- 2.0 General
- 3.0 Responsibility
- 4.0 Fabrication Plan

ATTACHMENTS:

- 1. BSC Fabrication Documents
- 2. Fabrication Flow Chart
- 3. Fabrication Priority List

Numbe

700

SPECIFICATION

Number

Rev.

Page 3 of 8

Number

1.0 PURPOSE

The purpose of this procedure is to define design guidelines, specifications, and procedures to enable PSI to specify, purchase, inspect, fabricate, test and ship the BSC chambers per LIGO requirements.

2.0 GENERAL

All Beam Splitter Chambers (BSC) shall be fabricated per this fabrication plan. Each fabrication process shall be controlled via a written procedure. A "first article" approach will be used to validate all fabrication processes prior to release of the full vessel lot.

All vessels will be fabricated in accordance with the Quality Plan. Key points in the fabrication process shall be verified to ensure consistent results.

All vacuum equipment shall be fabricated in accordance with LIGO Project Contract PC175730 dated September 12, 1995, and subsequent change orders.

3.0 RESPONSIBILITY

The Manufacturing Department is responsible for the execution of this procedure, with input and monitoring by the Project Engineer, the Quality Assurance Department, and the Project Manager.

4.0 FABRICATION PLAN

- 4.1 A first article approach (i.e. BSC prototype) will be used to start the BSC manufacturing cycle to validate the manufacturing procedures and technique prior to the full production release.
- 4.2 The BSC chambers will be fabricated using an outside manufacturing shop. PSI will perform vessel cleaning, leak checking, bakeout and preparation for shipment.
- 4.3 All BSC will be fabricated and tested per documents listed in Attachment I "Fabrication Documents".
- 4.4 The BSC will be fabricated and tested per Attachment 2 BSC Fabrication Flow Chart.
- 4.5 The BSC Chambers will be fabricated according to the Fabrication Priority List Attachment 3.

SPECIFICATION

Number A

V049-2-080

Rev.

FABRICATION PLAN FOR BEAM SPLITTER CHAMBERS (BSC)

4.6 Procurement

PSI will procure all S.S. plate and flange material and supply it with the selected fabrication vendor.

PSI will purchase vessel heads and supply them to the selected fabrication vendor.

4.7 Quality Assurance

The BSC Fabrication Process shall be monitored and control via the Quality Plan.

Outisde fabrication vendors will perform the quality plan inspections for their portion of the work. PSI will witness critical process inspections as detailed in the Quality Plan.

PSI will audit each major fabrication vendor's Q.A. Program after P.O. awards.

PSI and fabrication vendors will inspect all incoming materials to purchase documents.

4.8 Shop Conditioning/Testing

The Beam Splitter Chambers will be shop conditioned (cleaned, bakeout, etc.) per PSI Procedure V049-2-047.

4.9 Preparation For Shipment

The Beam Splitter Chambers will be prepared and shipped per PSI Procedure V049-2-123.

Numbe

HeV.

SPECIFICATION

Number A

Rev.

V049-2-080 Page _____ of __

PS-997

ATTACHMENT 1


BSC FABRICATION DOCUMENTS

		SPECIFICATION
	Floor Assembly	V049-4-036
	104.5" ID Flange	V049-4-022
	60 1/2" ID Flange (Grooved)	V049-4-019
	60" Port Cover	V049-4-014
	Chamber Supports	V049-4-023
	BSC Assembly	V049-4-001
18.	PSI Drawings	
17.	Component Packing, Handling, and Shipping Procedure	V049-2-123
16.	Dimensional Verification Procedure	V049-2-121
15.	Components Shop Conditioning/Test Plan	V049-2-047
14.	Leak Test Procedure	V049-2-014
13.	Bakeout Procedure	V049-2-019
12.	Stress Relief Procedures	V049-2-046
11.	Painting Procedures	V049-2-077
10.	Cleaning Procedures	V049-2-015
9.	Weld Repair Procedure	V049-2-074
8.	Weld Procedures	V049-2-070, V049-2-071, V049-2-072, V049-2-073
7.	Weld Data Sheet Spec.	V049-2-084
6.	Raw Material Handling Procedure	V049-2-120
5.	Heads	V049-2-039
4.	Flanges	V049-2-040 & V049-2-042
3.	Bill of Material	V049-4-001
2.	Spec. For Beam Splitter Chamber Quality Plan	V049-2-048
1.	Spec. For Beam Splitter Chamber (BSC)	V049-2-117

SPECIFICATION


Number

Rev.

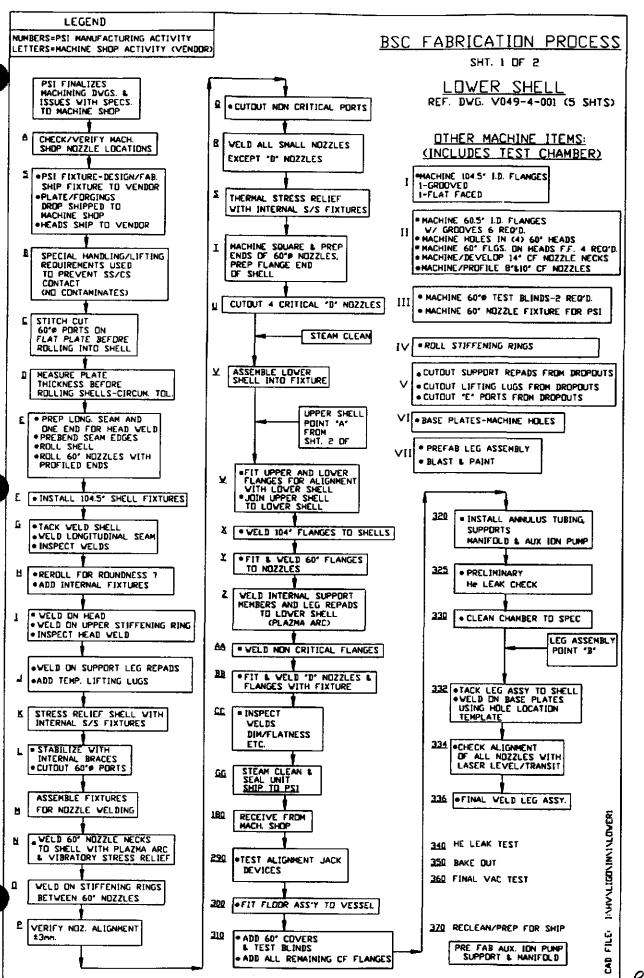

REVI Ø

PG 6 05 B

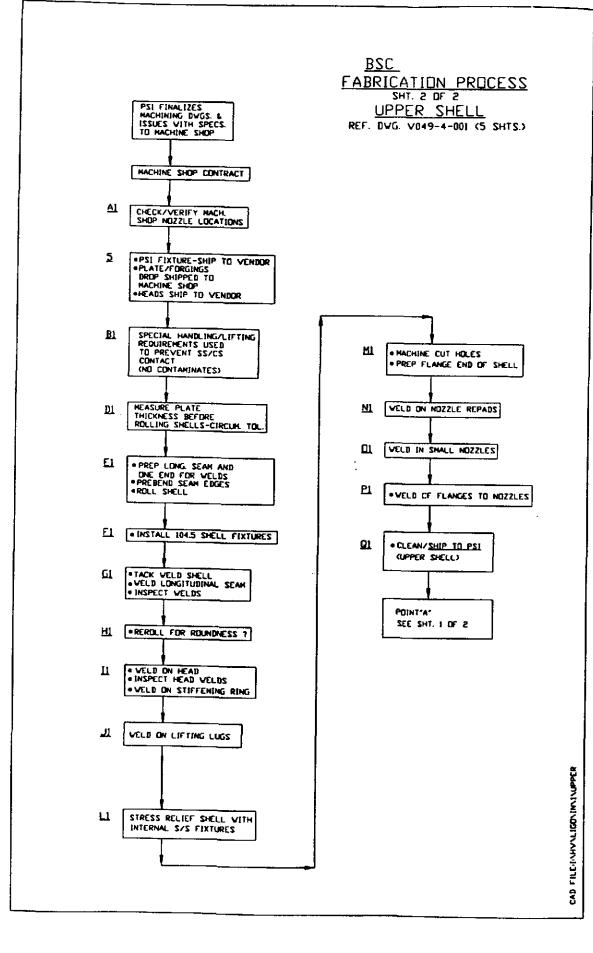

ATTACHMENT 3

BSC FABRICATION PRIORITY LIST

Prototype (Sp	are)
---------------	------

WBSC4 (CS)

WBSC7 (CS)

WBSC8 (CS)

WBSC1 (CS)

WBSC3 (CS)

WBSC2 (CS)

WBSC6 (LMS)

WBSC10 (LES)

WBSC5 (RMS)

WBSC9 (RES)

LBSC1 (CS)

LBSC3 (CS)

LBSC2 (CS)

LBSC5 (LES)

LBSC4 (RES)

SPECIFICATION

Number A

Rev.

Page _______ of ___

PS-997
